


**PHASE 3**  
(NO IMPACT TO TRAFFIC)

- CONSTRUCTION ACTIVITIES:
- 1) MOVE NORTHBOUND TRAFFIC BACK TO THE NATIVE NORTHBOUND LANES.
  - 2) REMOVE DETOUR.
  - 3) REMOVE TEMPORARY NORTHBOUND MEDIAN CROSSOVERS CONSTRUCTED IN PHASE 1.
  - 4) CONSTRUCT TEMPORARY SOUTHBOUND MEDIAN CROSSOVERS FOR USE IN PHASE 4.

**PHASE 4**  
(2 WEEK ANTICIPATED IMPACT TO TRAFFIC)

- CONSTRUCTION ACTIVITIES:
- 1) MOVE ALL TRAFFIC TO NORTHBOUND SIDE OF HIGHWAY VIA TEMPORARY MEDIAN CROSSOVERS BUILT IN PHASE 3.
  - 2) CLOSE MAIN STREET SOUTHBOUND OFF RAMP AND INDUSTRIAL ROAD SOUTHBOUND ON RAMP.
  - 3) IMPLEMENT DETOUR FOR LOCAL TRAFFIC.
  - 4) REMOVE EXISTING SOUTHBOUND BRIDGE.
  - 5) CONSTRUCT PROPOSED SOUTHBOUND ROADWAY OVER ARCH CULVERT CONSTRUCTED IN PHASE 1.

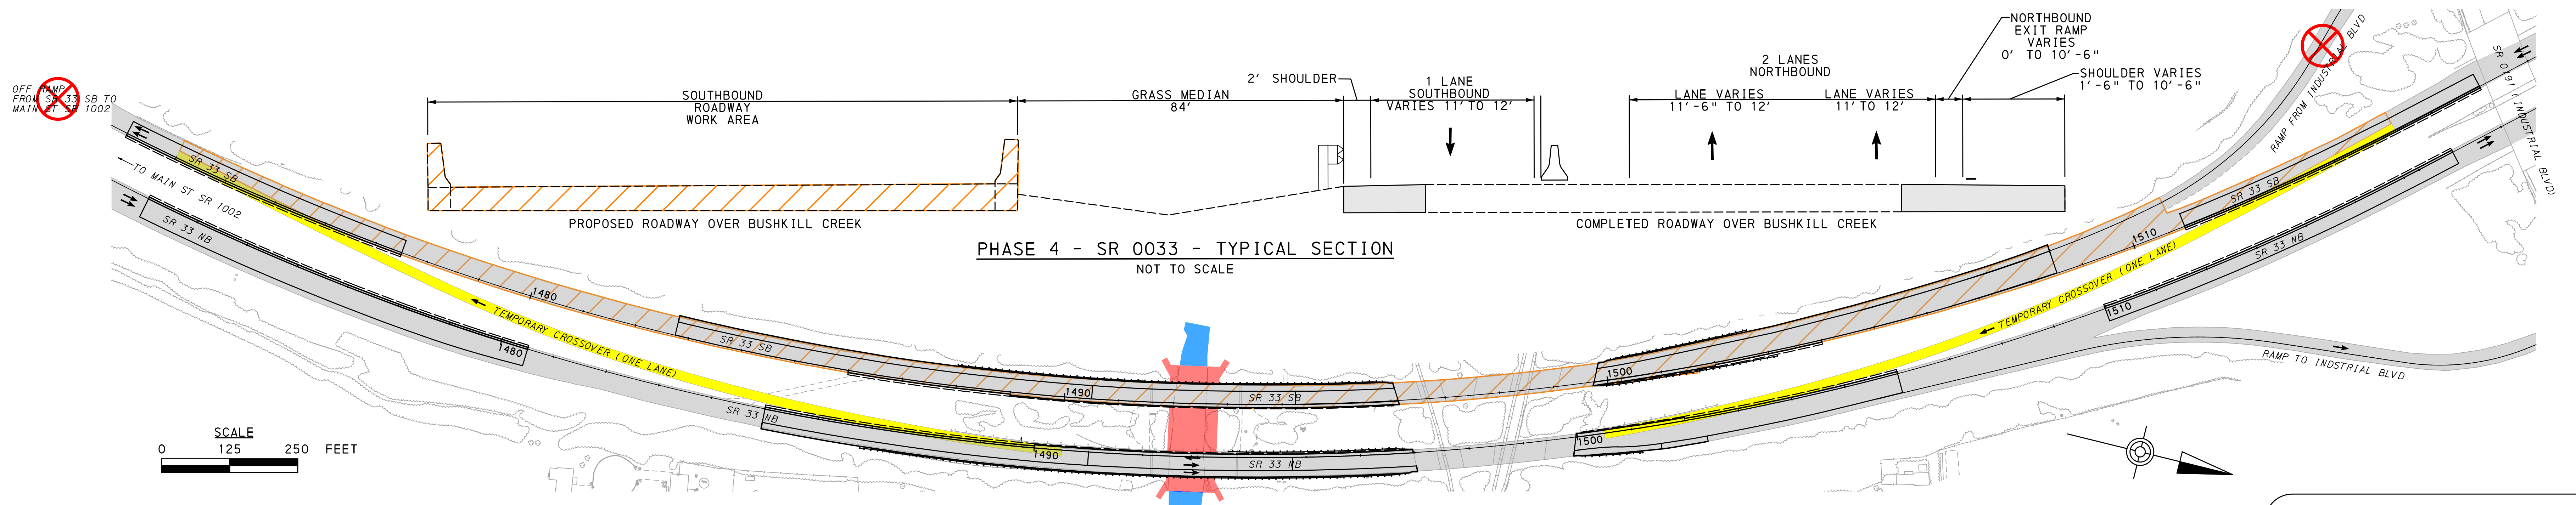

**LEGEND**

- TEMP MEDIAN CROSSOVER
- WORK AREA - ROAD CLOSED
- TEMP RAMP CLOSURE

**PHASE 5**  
(SHORT TERM IMPACT TO TRAFFIC DURING OFF-PEAK TIMES)

- CONSTRUCTION ACTIVITIES:
- 1) MOVE SOUTHBOUND TRAFFIC BACK TO THE NATIVE SOUTHBOUND LANES.
  - 2) REMOVE DETOUR.
  - 3) REMOVE TEMPORARY SOUTHBOUND MEDIAN CROSSOVERS CONSTRUCTED IN PHASE 3.
  - 4) CONSTRUCT FINAL PAVEMENT COURSE.
