


SR 33 SECTION 05B PALMER TOWNSHIP AND STOCKERTOWN BOROUGH NORTHAMPTON COUNTY BRIDGE REPLACEMENT PROJECT

PHASE 1 (NO IMPACT TO TRAFFIC)

- CONSTRUCTION ACTIVITIES:
- 1) CONSTRUCT PROPOSED ARCH CULVERT BENEATH EXISTING BRIDGES.
 - 2) CONSTRUCT TEMPORARY NORTHBOUND MEDIAN CROSSOVERS FOR USE IN PHASE 2.

PHASE 2 (2 WEEK ANTICIPATED IMPACT TO TRAFFIC)

- CONSTRUCTION ACTIVITIES:
- 1) MOVE ALL TRAFFIC TO SOUTHBOUND SIDE OF HIGHWAY VIA TEMPORARY MEDIAN CROSSOVERS BUILT IN PHASE 1.
 - 2) CLOSE MAIN STREET NORTHBOUND ON RAMP AND INDUSTRIAL ROAD NORTHBOUND OFF RAMP.
 - 3) IMPLEMENT DETOUR FOR LOCAL TRAFFIC.
 - 4) REMOVE EXISTING NORTHBOUND BRIDGE.
 - 5) CONSTRUCT PROPOSED NORTHBOUND ROADWAY OVER ARCH CULVERT CONSTRUCTED IN PHASE 1.

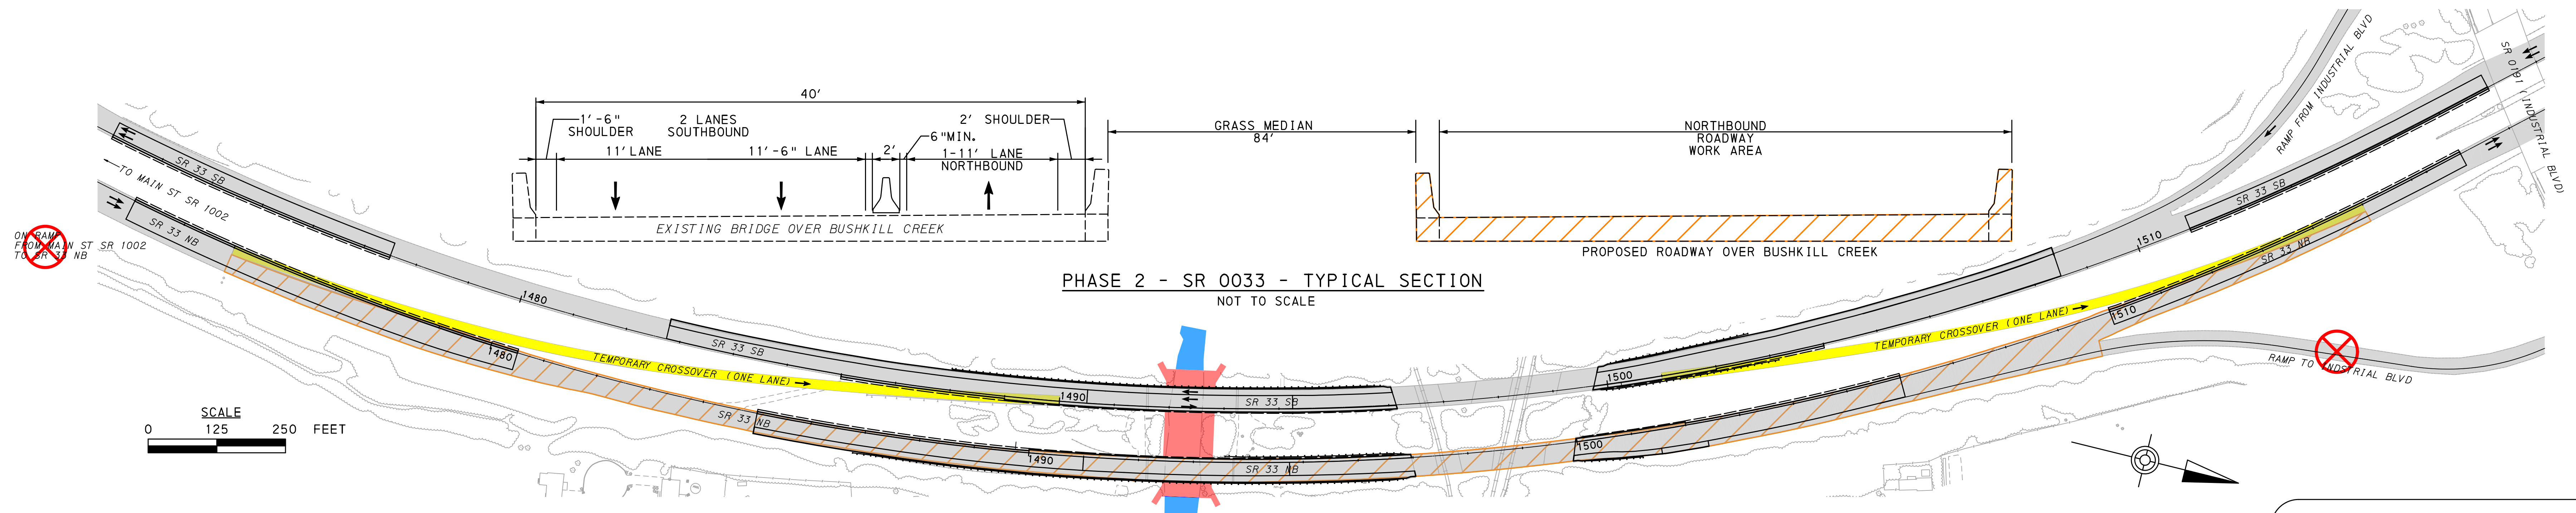

LEGEND

- TEMP MEDIAN CROSSOVER
- WORK AREA - ROAD CLOSED
- X TEMP RAMP CLOSURE

PHASE 3 (NO IMPACT TO TRAFFIC)

- CONSTRUCTION ACTIVITIES:
- 1) MOVE NORTHBOUND TRAFFIC BACK TO THE NATIVE NORTHBOUND LANES.
 - 2) REMOVE DETOUR.
 - 3) REMOVE TEMPORARY NORTHBOUND MEDIAN CROSSOVERS CONSTRUCTED IN PHASE 1.
 - 4) CONSTRUCT TEMPORARY SOUTHBOUND MEDIAN CROSSOVERS FOR USE IN PHASE 4.
